Original / Duplicate / Triplicate

CONTRACT CERTIFICATE

(For Other Works)

o. 1st & Part bill Date ..... 20 .....

ivision: Dasarahalli Project Division, Dasarahalli zone

ill Received No..... Dated..... Cash Book Voucher No..... dated .....

cheduled Docket No.....

ame of Work: Development of shettyhalli Burial Ground in S.No.55,56 and Deep land ward No 12 C

Category

ob Code No: 012-18-000045

ame of Contractor and Full Address : M/s KRIDL.

Work Order No: BBMP/EE/PD/WO-005/2018-19 Dated : 27/10/2018

ertified that the measurements were taken by me on 1.4.2021 and recorded in pages 251907 to 251917 f measurement Book No. 2520 and that the work is satisfactorily executed.

Officer-in-charge of work

Contractor

Certified that the measurements were taken by me on 1/4/2021 and found correct. The work is satisfactorily executed.

EXECUTIVE ENGINEER-4
KRIDL, BBMP DIVISON
BENGALURU-560 010

Certified that the quantities of materials shown in column 3 of Account II have been actually brought to site of the work and he contractor has not previously received any advance on this security. These materials are of an imperishable nature and re all required for immediate use on the work in connection with items for finished work have been agreed upon. A normal greement signed and executed by the contractor is recorded in the office.

Sub-Division Officer

f Memorandum of Payment 012-18-000045

1)	Total value of work done or supplies made as per account within	Gross 7239742-
2)	Deduct amount to be held in reserve being.....percent Rs.....	
3)	Deduct amount to be held in Balance	
4)	Deduct Payment :	
	a) Amount of previous payment as in the Office Cash Book Voucher No.....Dated.....S.D No.....	IT 144795-
	Amount adjusted towards cash advance recovery of	Lwc 72398-
	b) Payments cost store or other materials supplied.	CBF 7240-
	Now made recovery of amount creditable to this/other work	FSD 361987-
	Amount paid on this bill Cheque/Cash	Cust 64641-
5)	Balance being unpaid value of work done held in reserve	SgST 64641-
6)	Deduct cash advance made on the office Cash Book Voucher No..... date .....less adjustments	Ry 45298-
7)	Net amount due to or from contractor	Ded 761000-
	Unadjusted items	
8)	Advance to contractor for materials brought to site (as detailed) within value of Governme materials supplied	Net 6478742-

tractor's Signature

EXECUTIVE ENGINEER-4
KRIDL, BBMP DIVISON
BENGALURU-560 010

ved Rs.....(in words)

ish and by adjustment of Payment as per memorandum.

sses :

7239742-

(For use in the Office)

Audited and admitted for Rs. Seventy two lakhs thirty nine thousand seven hundred and forty two only

Passed by Cheque for Rs. ₹61,000/-

by accountancies

Accounts Superintendent

Exe. Engineer

B.B.M.P Dasarahalli Division

.....Signature of Contractor

EXECUTIVE ENGINEER-4
KRIDL, BBMP DIVISON
BENGALURU-560 010

me by cheque No.....Dated.....

.....Dated.....

als of Officer Making Payment

Executive Engineer

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
3	KSRB 2-2 : Earthwork excavation by manual means for foundation of buildings, water supply and sanitary lines and electrical conduits etc, either in pits or in trenches 1.5m and above in width, in soil not exceeding 1.5 m. in depth including dressing the bottom and sides of pits and trenches, stacking the excavated soil clear from edges of excavation with lead upto 50 m. including breaking of clods complete as per specifications.	Cum	900.91	332.34	299407.63	–	–	445.23	332.34	147968.27	445.23	147968.27
4	Earth work excavation for foundation of structures upto 3 mtrs. by mechanical means as per drawing and technical specification, including setting out, providing shoring, strutting and bracing, removal of stumps and other deleterious matter, dressing of sides and bottom, filling back the excavated earth to the extent required and utilising / transporting the remaining earth upto 1.00km lead. including cost of labour, materials and HOM etc. complete. do. Marshy soil	Cum	244.40	400.18	97803.99	–	–		400.18	0.00	0.00	0.00
5	KSRB 2.8 : Providing and Filling in foundation with granite / trap broken metal 100mm. and down size, with approved sand including hand packing, ramming, watering, including cost of all materials and labour with all lead and lift. complete as per specifications. specification.	Cum	105.69	2240.84	236833.26	–	–	45.89	2240.84	102831.03	45.89	102831.03

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
10	KSRB 4-6.1 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for foundations, footings, bases of columns for mass concrete including cost of all materials, labour complete as per specificaitons.	Sqm	753.00	310.58	233865.50	–	–	108.20	310.58	33603.51	108.20	33603.51
11	KSRB 4-6.3 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for flat surface such as suspended floors, roofs, landings, balconies and likes, thickness above 200 mm including cost of all materials, labour complete as per Specification. Specification.	Sqm	151.05	407.04	61483.39	–	–		407.04	0.00	0.00	0.00

Scanned by CamScanner

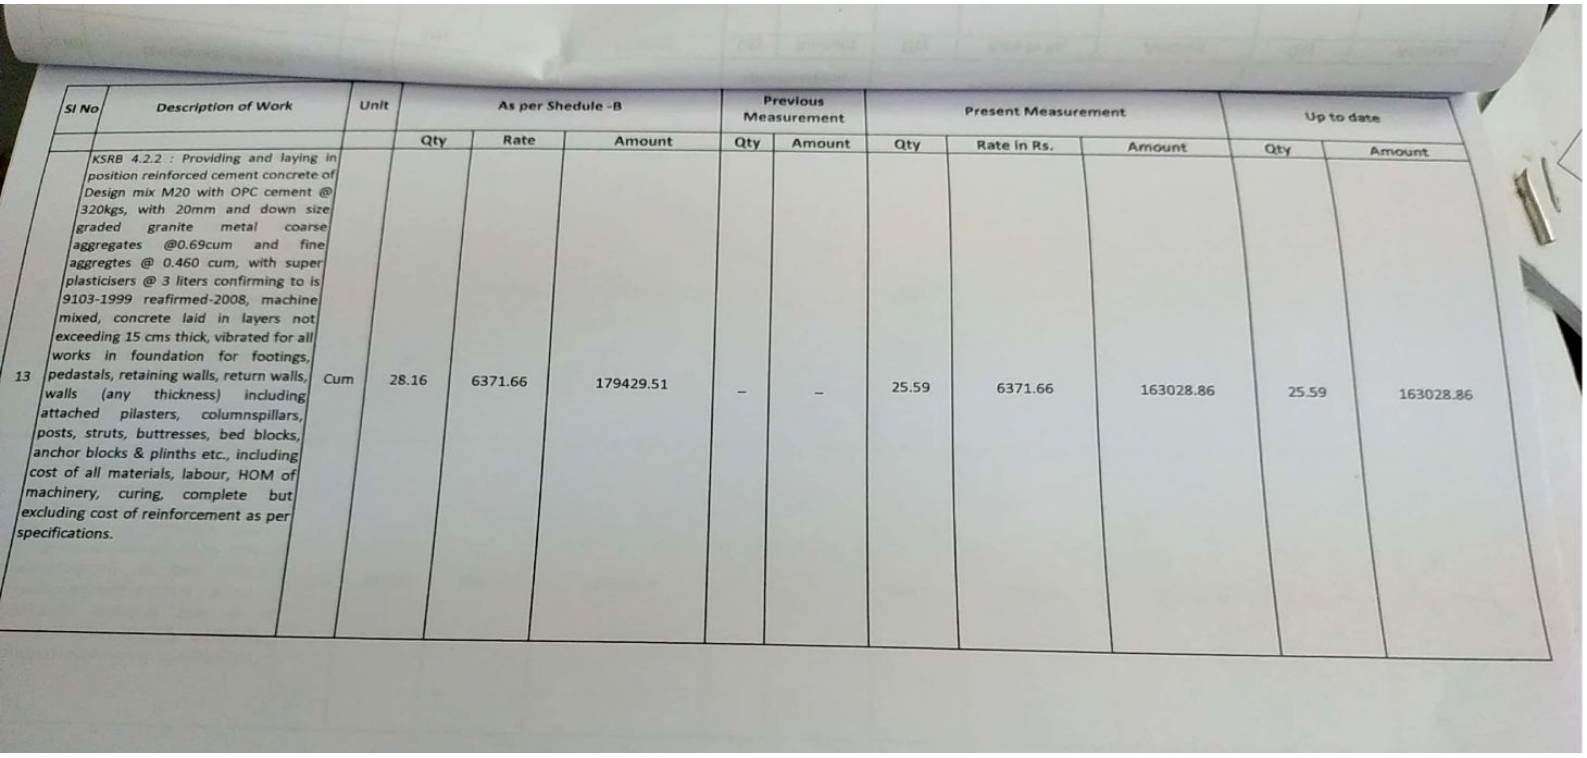

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
13	KSRB 4.2.2 : Providing and laying in position reinforced cement concrete of Design mix M20 with OPC cement @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregtes @ 0.460 cum, with super plasticisers @ 3 liters confirming to is 9103-1999 reafirmed-2008, machine mixed, concrete laid in layers not exceeding 15 cms thick, vibrated for all works in foundation for footings, pedastals, retaining walls, return walls, walls (any thickness) including attached pilasters, columnspillars, posts, struts, buttresses, bed blocks, anchor blocks & plinths etc., including cost of all materials, labour, HOM of machinery, curing, complete but excluding cost of reinforcement as per specifications.	Cum	28.16	6371.66	179429.51	–	–	25.59	6371.66	163028.86	25.59	163028.86

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
14	KSRB 4.9.2: Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with binding wire and anchoring to the adjoining members wherever necessary complete as per design (laps, hooks and wastage shall not be measured and paid) cost pf materials, labour, HOM of machinery complete as per specifications.Specification No. KBS 4.6.3 TMT bars Fe 500	Tn	14.59	64243.42	937298.84	–	–	1.57	64243.42	100936.23	1.57	100936.23
15	KSRB 5-11 : Providing and constructing load bearing wall with solid concrete blocks of size 400x200x200 mm having block density not lessthan 1800 kg/m3 and having a minimum average compressive strength 5.00 N/mm2 confirming to IS 2185 (Part) : 2005 and constructed with CM 1:4 , as per IS 2572:2005 including cost of all materials, labour charegs, scaffolding, curing complete as per specifications.	Sqm	369.87	993.22	367364.76			369.87	993.22	367364.76	369.87	367364.76

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
16	KSRB 4-1.6 ; Providing and laying in position plain cement concrete of mix 1:2:4 with cement @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.69 cum and fine aggregtes @ 0.459cum, machine mixed, concrete laid in layers not exceeding 15 cms. thick, well compacted, in foundation, plinth and cills, ncluding cost of all materials, labour, HOM of machinery, curing complete as per specifications.	Cum	4.05	5767.46	23338.60			4.05	5767.46	23338.60	4.05	23338.60
17	KSRB15-3.11 : Providing 20mm thick cement plaster in single coat with cement mortar 1:4, to stone masonry & concrete surface including rounding off corners wherever required smooth rendering, : Providing and removing scaffolding, including cost of materials, labour, curing complete as per specifications.	Sqm	765.25	248.04	189812.11			765.25	248.04	189812.11	765.25	189812.11
3	KSRB 15-16.1 : Providing and finishing external walls in two coats with waterproof cement paint of approved brand and shade to give an even shade after throughly brooming the surface to remove all dirt and loose powdered material, free from mortar drops and other foreign matter cost of materials, labour, complete as per specifications. : with primer.	Sqm	765.25	89.04	68137.68			765.25	89.04	68137.68	765.25	681

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
19	Providing and fixing M.S. Gate as per Chief Architect Drawing, using 50mm x 50mm 14 guage M.S. hollow pipe frame work bent to ornamental shape as shown in the drawing and 35mm x 6mm and 16 x 16mm Square rods for verticals alternatively spaced at 4cms c/c in two halves and 40mmx6mm M.S. flats for horizontal member and at the top cast iron spikes are provided at alternate vertical members asshown in the drawing etc., complete. All the steel surface should be thoroughly cleaned free of rust and painted with anti corrosive paint (shop paint) etc., complete. The work includes cost of all materials, labour charges for all items of work, hire charges for welding, cutting and grinding equipment, and electricity charges, with lead and lift, loading and unloading charges, etc., complete as per specifiocation.	Sqm	18.36	3110.04	57094.11			18.36	3110.04	57094.11	18.36	57094.11

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
21	KSRB 7.9 : Providing and fixing M.S. grill work for windows and ventilators weighing 21 kg/sqm using M.S. flats, or M.S. square rods, ro combination of M.S. flats and square rods as per approved design, drawing including cutting steel sections and welding the same to required pattern with a coat of red lead primer, cost of materials, fixtures, labour and and HOM of machinery complete as per specifications. Specification No. KBS 7.12.	Kg	133.65	84.24	11258.68			133.65	84.24	11258.68	133.65	11258.68
22	KSRB 15-18.2 : Providing and applying enamel metal paint two coats (excluding priming coat) over new steel or other metal surface brushing to give an even shade after cleaning oil, grease, dirt and other foreign matter, including cost of materials, labour, complete as per specifications.	Sqm	42.66	86.92	3707.66			42.66	86.92	3707.66	42.66	3707.66
23	Providing and fixing chlorinated poly venyl chloride (CPVC) pipes conforming to IS 15778 having thermal stability for hot and cold water supply including all CPVC plain and brass threaded fittings, this includes jointing of pipes and fittings with one step solvent cement, trenching, refilling & testing of joints complete,(external work)	m	422.00	486.00	205092.00			422.00	486.00	205092.00	422.00	205092.00

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
24	KSRB 13.11.1: Providing and placing on terrace. Polyethylene water storage tanks as per IS 12701 : 1996 with manhole lid and suitable locking arrangements, making holes of suitable diameter for inlet, outlet and over flow pipes, including cost of all materials, labour, transport charges, HOM of equipments and testing complete as per specifications. (For	Nos	1.00	9144.36	9144.36			1.00	9144.36	9144.36	1.00	9144.36
25	Fabricating supplying and erecting M.S. TubulerTruss of all span as per approved drawing design with prefabricated applications using quality material and are durable reliable and corrosion and abrasion resistant. welding shall confirm to latest structural welding code. Quality shall be on various parameters like shape, size, design gauge and polish. The entire trusses is anchored in RCC column by using 4 nos of M.S. anchor bolts at each support with 10mm thick base plate and shoe plate. The work includes cutting, straightening, placing in position of M.S. pipes and welding wherever necessary and applying one coat of redoxide primer coat to all the members including cost of all materials, labour charges of machineries for cutting, welding, grinding and erection equipments, with alllead and lift, transportation, etc, complete as per specification.	Kg	1096.76	118.80	130295.56			1096.76	118.80	130295.56	1096.76	130295.56
	Supplying and fixing new Mangalore tiles on existing reepers.	Sqm	86.92	392.04	34076.12			86.92	392.04	34076.12	86.92	34076.12

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
27	Providing Mangalore Ridge tiles set in C.M. 1:2 and pointed with C.M. 1:2.	m	48.00	190.08	9123.84			48.00	190.08	9123.84	48.00	9123.84
28	Providing corrugated cement asbestos Ridge sheets set in C.M. 1:3 and pointed with C.M. 1:3. including cost of materials, labour, HOM complete as per specifications.	m	24.00	470.88	11301.12			24.00	470.88	11301.12	24.00	11301.12
29	Geophysical investigation of site for sinking Borewell for supplying drinking water to the habitation either through the Hand pump, MWS of P.W.S.S by vertical electrical sounding by adopting Venner or Schlumberger's method, including reconnaissance survey of geological formation, Gerophysical investigation of existing Ground Wate in the vicinity, its qualityf 1.0 meter in consolidated formation for proper seating of casing pipe, depth of drilling required to cover full depth of aquifer proposed to be tapped, probable yield and other information required including transportation of instrument and accessories to work site., engaging techinical personal and labour required etc., as per Specification and	Nos	1.00	1938.46	1938.46			1.00	1938.46	1938.46	1.00	1938.46

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
31	Supply of ISI mark 175 mm nominal bore medium black ERW casing pipe of 5 mm thick black electric resistance continuous welded mild steel tube material confirming to IS 1387 / 1993 & manufactured from hot rolled steel skelp / stripes in random length of 4 to 7 mts both ends threaded confirming to IS 554 / 1985, one end fixed with a socket confirming to IS 4270 : 2001 and other end with Screwed pipes. All pipes shall be resonably free from defects. The tube shall be resonably stright should be with ISI marking, weighing 25.10 kg/m (inclusive of all taxes and durties). Prices include Collar medium duty material Component	m	44.00	1325.00	58300.00			29.00	1325.00	38425.00	29.00	38425.00
	Providing 175mm dia ms collar	Nos	2.00	150.00	300.00			2.00	150.00	300.00	2.00	300.00
	Providing 175mm dia bore cap CE(M)	Nos	1.00	100.00	100.00			1.00	100.00	100.00	1.00	100.00
	Supplying PVC pipes 100kg/Sqm 250mm Dia PVC (casing pipe)	Nos	50.00	2600.00	130000.00			50.00	2600.00	130000.00	50.00	130000.00
	Providing and fixing in trenches alvanised / mild steel tubes (medium ade) 50mm dia nominal bore with fittings (earth work in trenches to measured and paid for separately) uding cost of all materials, labour ges, HOM and testing complete as ecifications, Specification No.KBS 4 / 13.6	m	320.00	457.92	146534.40			320.00	457.92	146534.40	320.00	146534.40
	and delivery at site brand e, Suguna, CRI Kirloskar and equipment pumps 10.00 920 Stages)	Nos	1.00	50100.00	50100.00			1.00	50100.00	50100.00	1.00	50100.0

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
31	Supply of ISI mark 175 mm nominal bore medium black ERW casing pipe of 5 mm thick black electric resistance continuous welded mild steel tube material confirming to IS 1387 / 1993 & manufactured from hot rolled steel skelp / stripes in random length of 4 to 7 mts both ends threaded confirming to IS 554 / 1985, one end fixed with a socket confirming to IS 4270 : 2001 and other end with Screwed pipes. All pipes shall be resonably free from defects. The tube shall be resonably stright should be with ISI marking, weighing 25.10 kg/m (inclusive of all taxes and durties). Prices include Collar medium duty material Component	m	44.00	1325.00	58300.00			29.00	1325.00	38425.00	29.00	38425.00
32	Providing 175mm dia ms collar	Nos	2.00	150.00	300.00			2.00	150.00	300.00	2.00	300.00
3	Providing 175mm dia bore cap CE(M)	Nos	1.00	100.00	100.00			1.00	100.00	100.00	1.00	100.00
	Supplying PVC pipes 100kg/Sqm 250mm Dia PVC (casing pipe)	Nos	50.00	2600.00	130000.00			50.00	2600.00	130000.00	50.00	130000.00
	Providing and fixing in trenches galvanised / mild steel tubes (medium grade) 50mm dia nominal bore with ll fittings (earth work in trenches to e measured and paid for separately) cluding cost of all materials, labour arges, HOM and testing complete as specifications. Specification No.KBS 2.14 / 13.6	m	320.00	457.92	146534.40			320.00	457.92	146534.40	320.00	146534.40
	y and delivery at site brand bta, Suguna, CRI Kirloskar and equipment pumps 10.00 KV 920 Stages)	Nos	1.00	50100.00	50100.00			1.00	50100.00	50100.00	1.00	50100.00

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to Date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
37	Supplying and drawing 3 core flat PVC sheathed submersible pump cable manufactured with electrolytic grade copper with flexible copper with low resistance conductor confirming to table 3 class 5 of IS flexible copper conductor confirming to table 3 class 5 of IS:8130-1984 and virgin grade PVC insulation and powder coating extruded PVC sheathed suitable for working voltage upto 1100Volts as per IS-694:1990 & confirming to GTP of Group-A	m	360.00	126.70	45612.00			360.00	126.70	45612.00	360.00	45612.00
38	Providing and fixingin position 50mm nominal bore non-returnable valve vertical type of approved make including cost of all materials, labour and HOM of equipments with all leads complete as per specifications. Specification NO.KBS 13.2.10/13.13	Nos	1.00	1521.10	1521.10			1.00	1521.10	1521.10	1.00	1521.10
	Supplying and fixing 50mm GI Union	Nos	1.00	223.70	223.70			1.00	223.70	223.70	1.00	223.70
	Supplying and fixing 50mm GI Elbow	Nos	1.00	111.80	111.80			1.00	111.80	111.80	1.00	111.80
	Supplying and fixing 50mm GI Nipple	Nos	1.00	104.30	104.30			1.00	104.30	104.30	1.00	104.30
	Supplying and fixing 50mm GI Collar	Nos	1.00	103.00	103.00			1.00	103.00	103.00	1.00	103.00

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule - B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
43	Fabricating supplying and mounting MS box made out 14 SWG suitable for floor/wall mounting, fully weather proof provision for better heat dissipation proveded with hinged front cover equipped with tamper proof locking a arrangements with suitable size clamps with necessary cable entry pipe with glad and box should be finished with 2 coats of red oxide primer paint and finally finished with approved colour enamelled metal paint etc.., complete.	Sq cm	19900.00	0.37	7363.00			19900.00	0.37	7363.00	19900.00	7363.00
44	Supply and fixing angle iron grame work fabricated out of M.S angle iron. And M.S flat. With bolts, washers etc.., cand painted with 2 coats of red oxide and then 2 coats approved paint. 50x50x6mm	Nos	1.00	338.00	338.00			1.00	338.00	338.00	1.00	338.00
45	Supply of TPST with rewireable porcelain Channels in SM encloser. Made out of 14 SWG powder coated paint of approved colour. 32 amps	Nos	1.00	1868.00	1868.00			1.00	1868.00	1868.00	1.00	1868.00
5	Supplying and fixing 20"x20"x2.5" polished wood board made up not less than 15mm thick plank with front plank one end provided for olding at other end fixing the same of the valve using through bolts and nuts.	Nos	1.00	302.00	302.00			1.00	302.00	302.00	1.00	302.00
C	Supplying and fixing LED Type panel board indicating lamp with required olour suitable for 220V AC 50 Hz 1224	Nos	1.00	442.00	442.00			1.00	442.00	442.00	1.00	442.00

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -A			Previous Measurement		Present Measurement				
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
48	Supplying fully automatic star-delta starter unit push button type with suitable wires, 3 contactors, one adjustable thermal timer mounted on a common base plate held in steel enclosure for use on 400/440 volts 3 phase and wired after fixing to the existing wooden board for motor.Above 15 HP upto 25 HP	Nos	1.00	6583.00	6583.00			1.00	6583.00	6583.00	1.00	6583.00
49	Supplying and fixing single phase preventer using necessary wires over an existing panel board suitable for motor upto 20HP capacities.	Nos	1.00	768.00	768.00			1.00	768.00	768.00	1.00	768.00
50	Wiring for lighting/power circuit using one of FRLS PVC insulated 1100V grade multistrand copper conductor single core wire in open or concealed system of wiring as per IS 694: 1990 &confirming to the attached GTP of Group A 4mm Sqmm.	m	50.00	42.10	2105.00			50.00	42.10	2105.00	50.00	2105.00
51	Supplying fixing and wiring heavy duty low voltage capacitors conforming to IS 2834.3 Phase, 400/440 bolts gradem for power factor immprovement of rotating machinery.	Nos	5.00	414.00	2070.00			5.00	414.00	2070.00	5.00	2070.00

Scanned by CamScanner

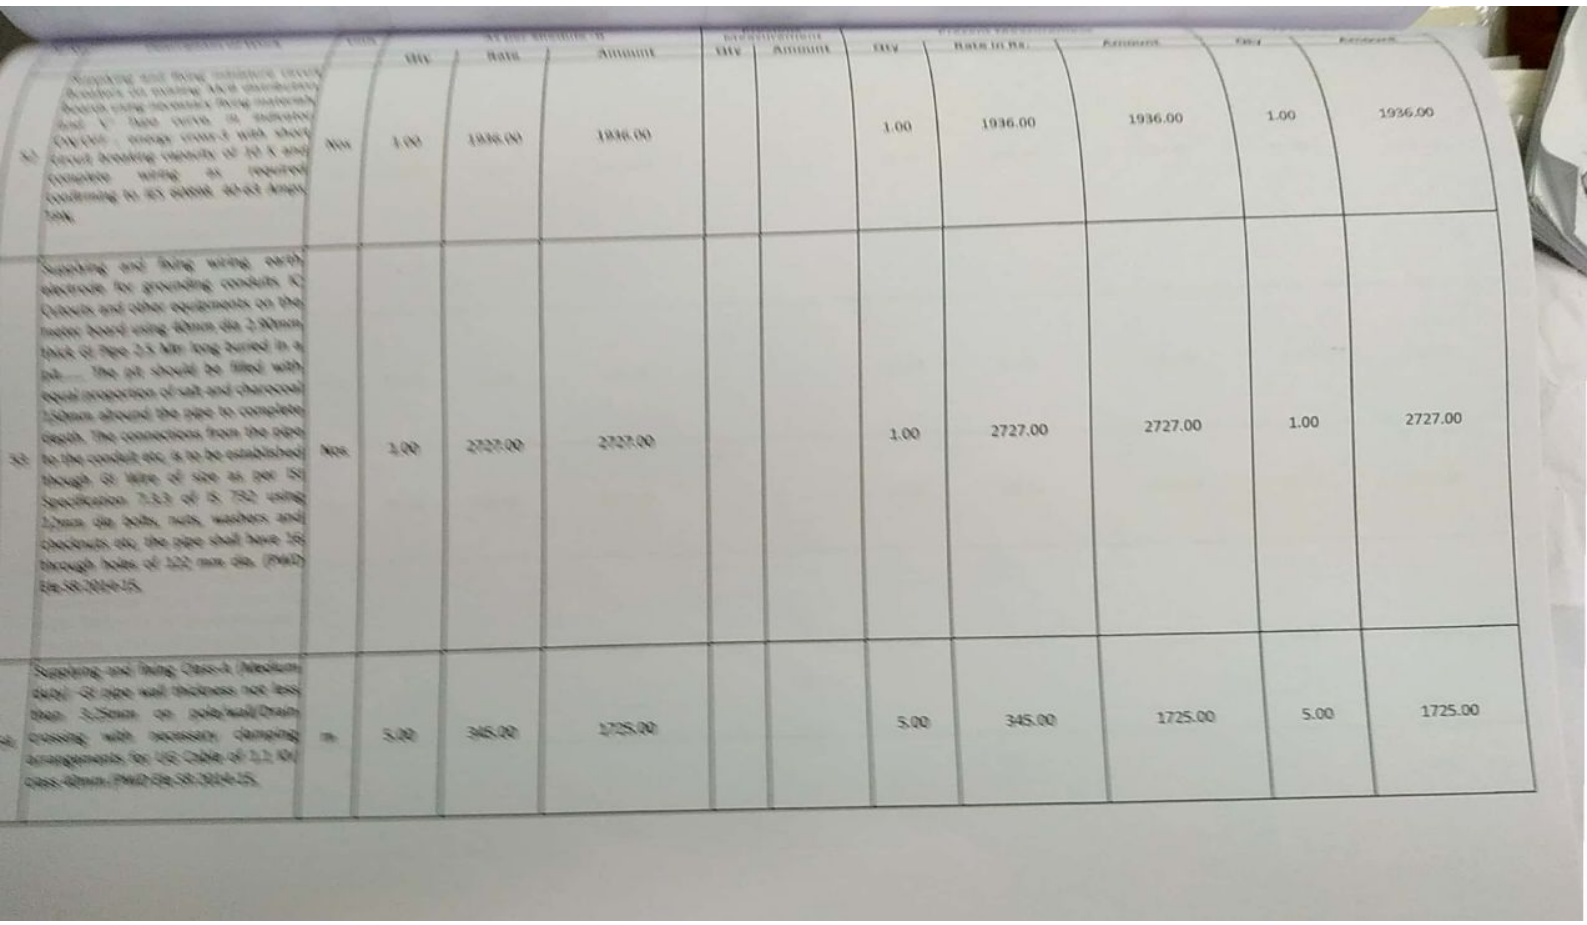

			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
32	Supplying and fixing industrial circuit breakers on existing MCB distribution boards using necessary fixing materials and 'C' type curve, 16 industrial DB(16A , energy class-3 with short circuit breaking capacity of 10 K and complete wiring as required conforming to IS 60898, 40-63 Amps, 2pole.	Nos	1.00	1936.00	1936.00			1.00	1936.00	1936.00	1.00	1936.00
33	Supplying and fixing wiring earth electrode for grounding conduits, DB, Outlets and other equipments on the meter board using 40mm dia 2.90mm thick GI Pipe 2.5 Mtr long buried in a pit..... The pit should be filled with equal proportion of salt and charcoal 150mm around the pipe to complete depth. The connections from the pipe to the conduit etc, is to be established through GI Wire of size as per IS Specification 7.3.3 of IS 732 using 12mm dia bolts, nuts, washers and checknuts etc, the pipe shall have 16 through holes of 12.2 mm dia. (PWD Elc.SR:2016-17).	Nos.	1.00	2727.00	2727.00			1.00	2727.00	2727.00	1.00	2727.00
	Supplying and fixing Class-A (Medium duty) GI pipe wall thickness not less than 3.25mm on pole/wall/Drain crossing with necessary clamping arrangements for UG Cable of 3.5 /0 core 40mm.(PWD Elc.SR:2016-17).	m	5.00	345.00	1725.00			5.00	345.00	1725.00	5.00	1725.00

Scanned by CamScanner

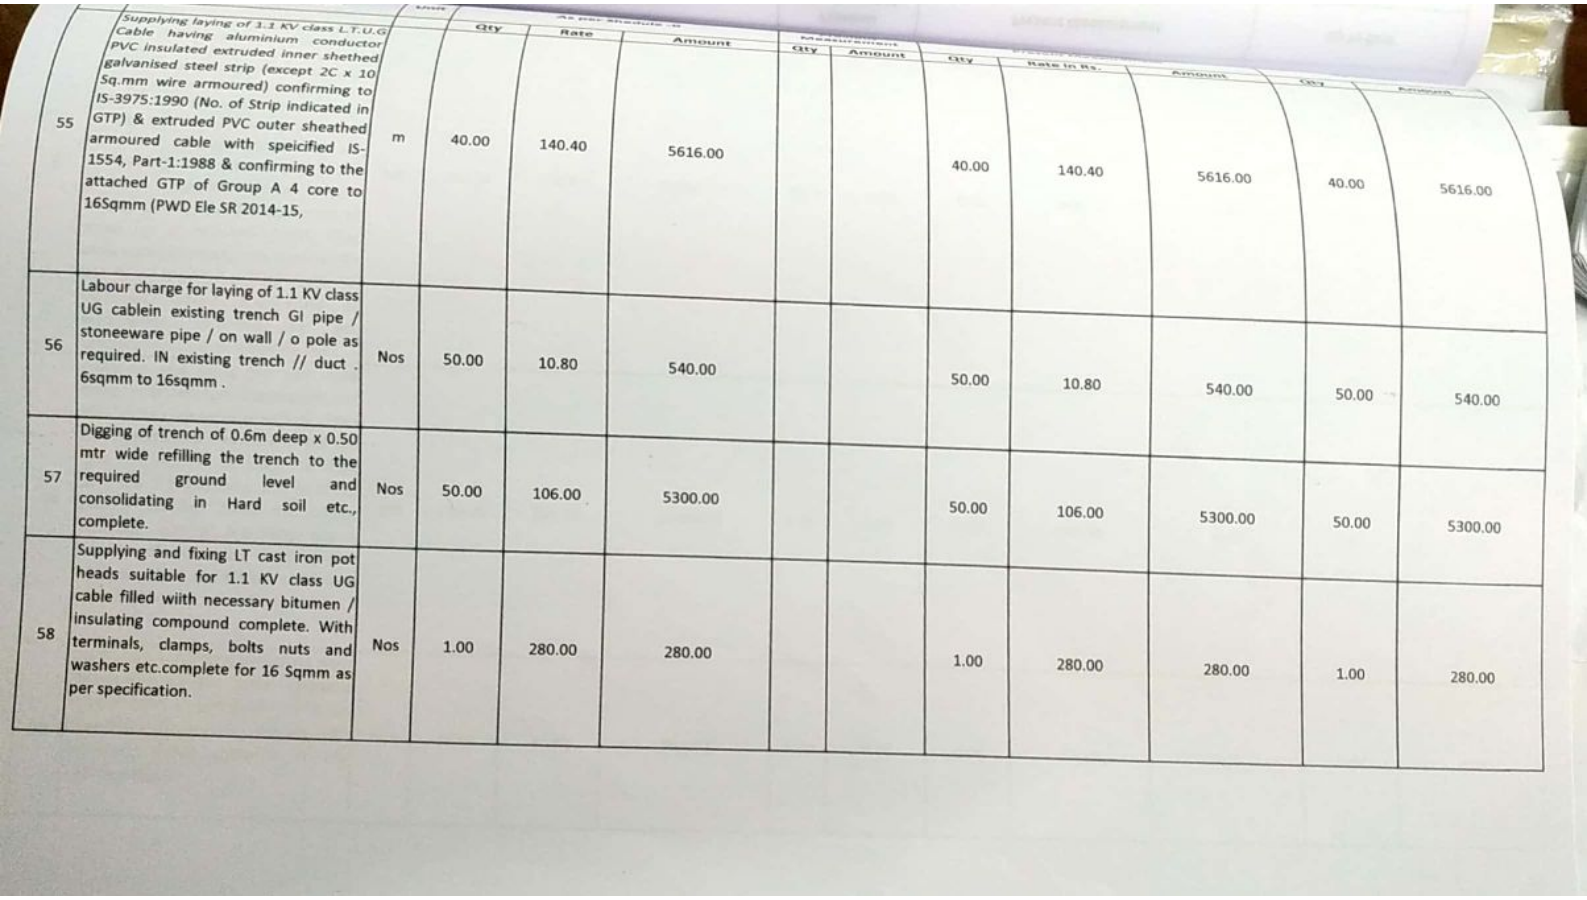

			As per schedule of			Measurement							
		Unit	Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
55	Supplying laying of 1.1 KV class L.T.U.G Cable having aluminium conductor PVC insulated extruded inner shethed galvanised steel strip (except 2C x 10 Sq.mm wire armoured) confirming to IS-3975:1990 (No. of Strip indicated in GTP) & extruded PVC outer sheathed armoured cable with speicified IS-1554, Part-1:1988 & confirming to the attached GTP of Group A 4 core to 16Sqmm (PWD Ele SR 2014-15,	m	40.00	140.40	5616.00			40.00	140.40	5616.00	40.00	5616.00
56	Labour charge for laying of 1.1 KV class UG cablein existing trench GI pipe / stoneeware pipe / on wall / o pole as required. IN existing trench // duct . 6sqmm to 16sqmm .	Nos	50.00	10.80	540.00			50.00	10.80	540.00	50.00	540.00
57	Digging of trench of 0.6m deep x 0.50 mtr wide refilling the trench to the required ground level and consolidating in Hard soil etc., complete.	Nos	50.00	106.00	5300.00			50.00	106.00	5300.00	50.00	5300.00
58	Supplying and fixing LT cast iron pot heads suitable for 1.1 KV class UG cable filled wiith necessary bitumen / insulating compound complete. With terminals, clamps, bolts nuts and washers etc.complete for 16 Sqmm as per specification.	Nos	1.00	280.00	280.00			1.00	280.00	280.00	1.00	280.00

Scanned by CamScanner

Sl No	Description of Work	Unit	As per Shedule -B			Previous Measurement		Present Measurement			Up to date	
			Qty	Rate	Amount	Qty	Amount	Qty	Rate in Rs.	Amount	Qty	Amount
73	Supply & fixing of Pull Down Challenger : All products must tested and certified to meet EN16630 safety standards with GS test mark. The EN16630 certificates must be issued by a reputed notified International Certifying Body such as IPEMA, TUV, CPSC, or SGS only. The GS mark-EN 16630 certificates must be in the name of a supplier who has carried out a minimum of 100 public park projects in India with EN16630-GS certified products either by themselves or through their dealers or contractors. These EN16630 & GS Mark certificates must be clearly displayed on the notified certifying bodies websites as online verification is mandatory during technical bid. All products must clearly display the GS mark as has been issued	Nos	1.00	296000.00	296000.00				296000.00	0.00	0.00	0.00
74	Supplying and fixing Porcelain fuse channel with cut out on the existing wooden / panel using necessary nuts , bolrs and washers. 63 Amps.	Nos	4.00	234.00	936.00			4.00	234.00	936.00	4.00	936.00
75	BESCOM Deposit charges and miscellanesous	Nos	3.00	15000.00	45000.00				15000.00	0.00		0.00
	Total				**12004432.00**					**6522290.88**		**652229**0.88
	KRIDL Charges				**1320487.52**					**717452.00**		**71745**2.00
	Grand Total				**13324919.52**					**7239742.87**		**723974**2.87

CERTIFICATE

1 Certified that the work done is satisfactorily.

2 There is no departmental issues by BBMP

Assistant Engineer
Project Division Dasarahalli
BBMP Bangalore

Asst. Executive Engineer,
Project Division Dasarahalli
BBMP Bangalore

Scanned by CamScanner
